


Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	2020												2021												2022												2023																							
						D	J	F	M	A	M	J	Jul	A	S	O	N	D	D	J	F	M	A	M	J	Jul	A	S	O	N	D	D	J	F	M	A	M	J	Jul	A	S	O	N	D	D	J	F																		
JACOBY - Update 16 Jacoby Creek Bridge - Schedule Update 16 - F																																																																	
JACOBY - Update 16.1 Milestones																																																																	
1000	Contract Approval	0		14-Feb-20A	02-Nov-22A																																																												
1010	Begin Work	0		01-Jun-20A																																																													
2010	GSB Float	2		02-Nov-22A	02-Nov-22A																																																												
2020	Caltrans Float	0		02-Nov-22A	02-Nov-22A																																																												
3000	Project Complete	0																																																															
JACOBY - Update 16.2 Submittals																																																																	
JACOBY - Update 16.2.1 Roadway & Environmental																																																																	
10000	Submit Biologist Resume & SOQ	5		27-Feb-20A	02-Mar-20A																																																												
10010	Review/Authorize Biologist Resume & SOQ	15		02-Mar-20A	04-Mar-20A																																																												
10020	Prepare Baseline Schedule	10		24-Feb-20A	03-Mar-20A																																																												
10020 R1	Revise Baseline Schedule	5		23-Mar-20A	24-Mar-20A																																																												
10020 R2	Revise Baseline Schedule	5		24-Mar-20A	25-Mar-20A																																																												
10030	Review/Authorize Baseline Schedule	20		03-Mar-20A	23-Mar-20A																																																												
10030 R1	Review/Authorize Baseline Schedule	5		24-Mar-20A	24-Mar-20A																																																												
10030 R2	Review/Authorize Baseline Schedule	5		25-Mar-20A	03-Apr-20A																																																												
10040	Prepare SWPPP	15		19-Mar-20A	02-Apr-20A																																																												
10040 R1	Prepare SWPPP R1	5		07-Apr-20A	08-May-20A																																																												
10040 R2	Prepare SWPPP R2	5		08-May-20A	13-May-20A																																																												
10050	Review/Authorize SWPPP	15		02-Apr-20A	07-Apr-20A																																																												
10050 R1	Review/Authorize SWPPP R1	5		08-May-20A	08-May-20A																																																												
10050 R2	Review/Authorize SWPPP R2	5		13-May-20A	13-May-20A																																																												
10060	Provide DRA Nomination/Disclosures by GSB & CT	5		20-Feb-20A	28-Apr-20A																																																												
10070	Select DRA for Project	15		28-Apr-20A	28-Apr-20A																																																												
10080	Prepare Traffic Closure Contingency Plan	5		15-May-20A	18-May-20A																																																												
10090	Review/Authorize Traffic Closure Contingency Plan	15		18-May-20A	23-Jun-20A																																																												
10100	Prepare Hydroacoustic Monitoring Plan	10		16-Mar-20A	26-Mar-20A																																																												
10100 R1	Prepare Hydroacoustic Monitoring Plan R1	5		30-Apr-20A	13-May-20A																																																												
10110	Review/Authorize Hydroacoustic Monitoring Plan	14		26-Mar-20A	30-Apr-20A																																																												
10110 R1	Review/Authorize Hydroacoustic Monitoring Plan R1	5		13-Apr-20A	23-Jun-20A																																																												
10120	Prepare Natural Resources Protection Plan	7		19-Mar-20A	26-Mar-20A																																																												
10130	Review/Authorize Natural Resource Protection Plan	15		26-Mar-20A	30-Apr-20A																																																												
10140	Prepare Invasive Species Control Plan	10		16-Mar-20A	24-Mar-20A																																																												
10150	Review/Authorize Invasive Species Control Plan	15		24-Mar-20A	24-Mar-20A																																																												
10160	Prepare Bat and Bird Exclusion Plan	10		30-Mar-20A	07-Apr-20A																																																												
10170	Review/Authorize Bat and Bird Exclusion Plan	10		07-Apr-20A	09-Apr-20A																																																												
10180	Prepare Lead Compliance Plan - Stripe Removal	20		13-Apr-20A	22-Apr-20A																																																												
10180 R1	Prepare Lead Compliance Plan - Stripe Removal R1	5		29-Apr-20A	06-May-20A																																																												
10190	Review/Authorize Lead Compliance Plan - Stripe Removal	7		22-Apr-20A	29-Apr-20A																																																												
10190 R1	Review/Authorize Lead Compliance Plan - Stripe Removal R1	5		06-May-20A	06-May-20A																																																												
10200	Prepare Lead Compliance Plan -ADL Soil Excavation	15		26-Feb-20A	11-Mar-20A																																																												
10200 R1	Revise Lead Compliance Plan -ADL Soil Excavation	5		13-Mar-20A	16-Mar-20A																																																												
10210	Review/Authorize Lead Compliance Plan -ADL Soil Excavation	7		11-Mar-20A	13-Mar-20A																																																												
10210 R1	Review/Authorize Lead Compliance Plan -ADL Soil Excavation	5		16-Mar-20A	24-Mar-20A																																																												

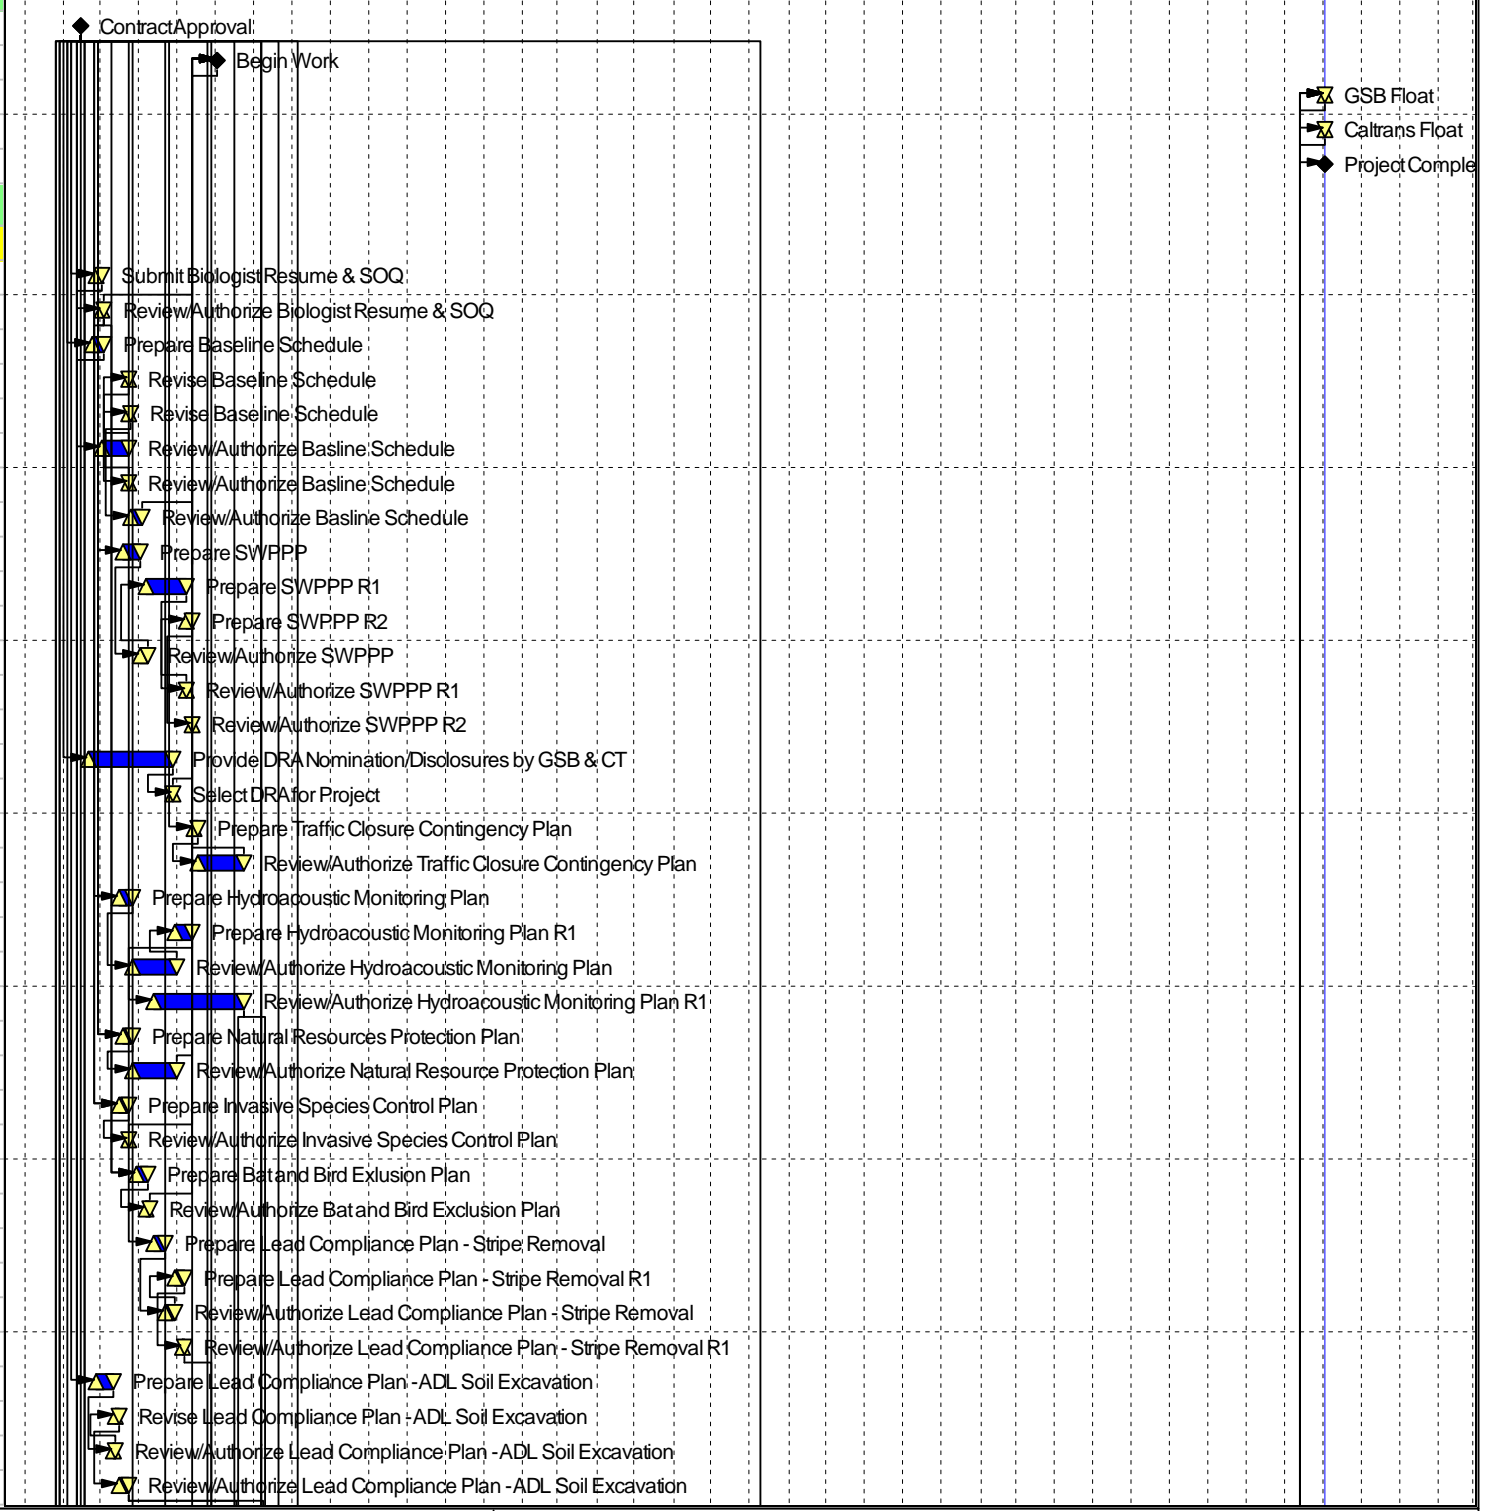

- ◆ GSB Float
- ◆ Caltrans Float
- ◆ Project Complete

▶ Remaining Level of Effort
 ▶ Actual Work
 ▶ Critical Remaining Work
▶ Actual Level of Effort
 ▶ Remaining Work
 ◆ Milestone

Activity ID	Activity Name	Original Duration	Total Float	Start	Finish	2020												2021												2022												2023	
						D J F M A M J Jul A S O N D												D J F M A M J Jul A S O N D												D J F M A M J Jul A S O N D												D J	
23040	Prepare Overhang Forming Design - Jacoby & Gannon Rt	20		09-Mar-20A	16-Mar-20A																																						
23040 R1	Prepare Overhang Forming Design - Jacoby & Gannon Rt R1	5		06-Apr-20A	07-Apr-20A																																						
23050	Review/Authorize Overhang Forming Design - Jacoby & Gannon Rt	20		16-Mar-20A	05-Apr-20A																																						
23050 R1	Review/Authorize Overhang Forming Design - Jacoby & Gannon Rt R1	5		07-Apr-20A	07-Apr-20A																																						
JACOBY - Update 16.2.2.4 Methods		219		14-Feb-20A	16-Mar-21A																																						
24000	Prepare Pile Handling Plan	15		15-Jun-20A	22-Jun-20A																																						
24010	Review/Authorize Pile Handling Plan	15		22-Jun-20A	23-Jun-20A																																						
24020	Prepare Pile Driving System Submittal	5		14-Feb-20A	20-Feb-20A																																						
24030	Review/Authorize Pile Driving System Submittal	15		20-Feb-20A	06-Mar-20A																																						
24040	Prepare Precast Girder Erection Plan	10		11-May-20A	21-May-20A																																						
24050	Review/Authorize Precast Girder Erection Plan	20		21-May-20A	04-Jun-20A																																						
24080	Prepare Deck Placement Plan	10		06-Jul-20A	13-Jul-20A																																						
24090	Review/Authorize Deck Placement Plan	15		13-Jul-20A	25-Aug-20A																																						
24100	Prepare Bridge Move Shop Drawings	20		06-Mar-20A	09-Jun-20A																																						
24100 R1	Prepare Bridge Move Shop Drawings R1	20		26-Jun-20A	13-Sep-20A																																						
24100 R2	Prepare Bridge Move Shop Drawings R2	5		09-Feb-21A	19-Feb-21A																																						
24100 R3	Prepare Bridge Move Shop Drawings R3	5		04-Mar-21A	09-Mar-21A																																						
24110	Review/Authorize Bridge Move Shop Drawings	20		09-Jun-20A	26-Jun-20A																																						
24110 R1	Review/Authorize Bridge Move Shop Drawings R1	20		13-Sep-20A	09-Feb-21A																																						
24110 R2	Review/Authorize Bridge Move Shop Drawings R2	5		19-Feb-21A	04-Mar-21A																																						
24110 R3	Review/Authorize Bridge Move Shop Drawings R3	5		09-Mar-21A	16-Mar-21A																																						
24120	Prepare Bridge Move Work Plan	20		27-Jul-20A	13-Sep-20A																																						
24120 R1	Prepare Bridge Move Work Plan R1	5		09-Feb-21A	19-Feb-21A																																						
24120 R2	Prepare Bridge Move Work Plan R2	5		26-Feb-21A	01-Mar-21A																																						
24130	Review/Authorize Bridge Move Work Plan	20		13-Sep-20A	09-Feb-21A																																						
24130 R1	Review/Authorize Bridge Move Work Plan R1	5		19-Feb-21A	26-Feb-21A																																						
24130 R2	Review/Authorize Bridge Move Work Plan R2	5		01-Mar-21A	16-Mar-21A																																						
24140	Prepare Bridge Move Contingency Plan	20		27-Jul-20A	13-Sep-20A																																						
24140 R1	Prepare Bridge Move Contingency Plan R1	5		09-Feb-21A	19-Feb-21A																																						
24140 R2	Prepare Bridge Move Contingency Plan R2	5		26-Feb-21A	01-Mar-21A																																						
24150	Review/Authorize Bridge Move Contingency Plan	20		13-Sep-20A	09-Feb-21A																																						
24150 R1	Review/Authorize Bridge Move Contingency Plan R1	5		19-Feb-21A	26-Feb-21A																																						
24150 R2	Review/Authorize Bridge Move Contingency Plan R2	5		01-Mar-21A	16-Mar-21A																																						
24160	Prepare Bridge Move Geometric Plan	10		27-Jul-20A	13-Sep-20A																																						
24160 R1	Prepare Bridge Move Geometric Plan R1	5		09-Feb-21A	19-Feb-21A																																						
24170	Review/Authorize Bridge Move Geometric Control Plan	20		13-Sep-20A	09-Feb-21A																																						
24170 R1	Review/Authorize Bridge Move Geometric Control Plan R1	5		19-Feb-21A	16-Mar-21A																																						
JACOBY - Update 16.2.2.5 Permanent Materials		132		02-Mar-20A	17-Aug-20A																																						
25000	Prepare Precast QC Plan	20		02-Mar-20A	10-Mar-20A																																						
25010	Review/Authorize Precast QC Plan	15		10-Mar-20A	04-Apr-20A																																						
25020	Prepare Precast Girder Shop Drawings	20		02-Mar-20A	24-Mar-20A																																						
25020 R1	Prepare Precast Girder Shop Drawings R1	5		14-Apr-20A	22-Apr-20A																																						
25030	Review/Authorize Precast Girder Shop Drawings	20		24-Mar-20A	14-Apr-20A																																						
25030 R1	Review/Authorize Precast Girder Shop Drawings R1	5		22-Apr-20A	04-May-20A																																						
25040	Prepare Prestress Shop Drawings	20		09-Mar-20A	19-Mar-20A																																						

TASK filter: All Activities

